



DPM FTE Calculator

User Guide

How to estimate the DPM effort and full-time people a WAN or LAN rollout needs — step by step, with every screen explained. Written for Delivery Project Managers; no spreadsheet or training required.

Version 2.3.0

Network Estimator · Orange

What's inside

1. Welcome & the key ideas

What the tool does, and the five words you need: MD, FTE, headcount, utilisation, scenario.

2. Your first WAN estimate

Describe the project, allocate the sites, read the result.

3. A LAN estimate

Device tiers, the three calculation modes, and delivery stages.

4. Comparing scenarios

Weigh the same project under different conditions, side by side.

5. Records & projects

Everything you calculate is saved; reopen, review and reload it.

6. Team capacity

All active estimates on one calendar, against the size of the team.

7. The DPM directory

The people you can assign to an estimate.

8. Rates & method

Where the numbers come from, and a glossary.

9. Saving to the SharePoint team folder

How the team shares one set of estimates automatically.

10. Keeping the app up to date

The "what's new" panel and one-click updates.

The five words

MD — man-day

One person working one full day. Every effort in the tool is in man-days.

FTE

Full-time equivalent: $\text{man-days per month} \div \text{one DPM's monthly capacity (18 MD by default)}$.

Headcount

FTE rounded up to whole people. 0.86 FTE still needs 1 person.

Utilisation

$\text{FTE} \div \text{headcount}$ — how fully the rounded-up team is loaded.

WAN vs LAN

Two estimators. WAN is priced per product & connectivity mode; LAN per device-count tier.

Record vs project

A *record* is a saved result. A *project* is saved inputs you can reload.

1 Welcome & the key ideas

The DPM FTE Calculator turns a project's size into the effort and the number of full-time people it needs — consistently, and with the arithmetic shown so anyone can follow it.

You describe a rollout (how long it runs, how many sites, what products or device tiers), and the tool returns the total **man-days**, the **FTE**, the **headcount** and the **utilisation**, along with how the effort spreads across the months. Every calculation is saved automatically, and — when the team folder is linked — shared with your colleagues.

The home screen

The sidebar on the left is how you move around: the two estimators (**WAN**, **LAN**), the **Team capacity** plan, your saved **FTE Records** and **Projects**, the **DPM Directory**, and **Rates & Method**. The **Dashboard** opens with what the latest version added and a summary of your most recent estimate.

Dashboard Saving to data folder LAN · 2.58 FTE · 418.8 MD

What's new in version 2.3.0 new Check for updates

Compare scenarios side by side · released Oct 01, 2026

- Compare scenarios: run several estimates of the same project side by side under different conditions - complexity, mode, flat or bell curve, migration, duration, capacity, the allocation - and see how the man-days and FTE change, with the differences highlighted and the change against the first scenario shown.
- Add a scenario with one click on the WAN or LAN page. Nothing is written to the data folder while you experiment; load any scenario back to tweak it.
- Save the one you want as the estimate, or save the whole comparison in your browser to reopen later.

✓ You have the latest version. Last checked 12:54 PM. Got it All updates

Dashboard

The most recent WAN and LAN estimates, and how the effort is spread across the project calendar.

LATEST WAN ESTIMATE

TOTAL MAN-DAYS ⓘ 186.3 80 sites over 12 months	MAN-DAYS PER MONTH ⓘ 15.5 Sustained monthly workload
FTE REQUIRED ⓘ 0.86 At 18 MD per DPM per month	HEADCOUNT ⓘ 1 × 86.2% People needed and how loaded they are

Switch to dark

The Dashboard. A “what’s new” panel at the top, then the headline figures from your latest WAN and LAN estimates.

Where do I start?

Pick **WAN Estimator** or **LAN Estimator** from the sidebar depending on the rollout. The next two chapters walk through each.

2 Your first WAN estimate

A WAN estimate prices wide-area rollouts per site, from the product and the connectivity mode.

Step 1 — Describe the project

1. Give the project a **name**. A stable project code (e.g. `DPM-ALS-U4R6`) appears top-right and stays with it.
2. Set the **duration** — type a number of months, or switch to **Start / end date** and let the tool work it out.
3. Optionally set a **planned start** month (this places the project on the Team-capacity calendar; it does not change the FTE).
4. Choose the **effort distribution**: **Flat** spreads the work evenly; **Bell curve** ramps up to a mid-project peak and reports the extra **Peak FTE** that peak needs.

The screenshot displays the 'WAN Estimator' tool interface. On the left is a dark sidebar with navigation links: DPM FTE NETWORK ESTIMATOR, ESTIMATE (Dashboard, WAN Estimator, LAN Estimator), PLAN (Team capacity), DATA (FTE Records, Projects, DPM Directory), and HELP (Rates & Method, Settings). A 'Switch to dark' toggle is at the bottom. The main panel has a header with 'WAN Estimator', a 'Saving to data folder' status, and a summary 'WAN · 0.52 FTE · 56.3 MD'. Below the header, the 'PROJECT INFORMATION' section includes: Project name 'Acme Logistics — SD-WAN' (code DPM-ALS-U4R6), Project status 'Active' (team plan only), DPM acting as PM 'No' (recorded only), Duration '6 months' (Start / end date), Duration in months '6', Planned start 'February 2026' (for the team plan), and Effort distribution 'Flat (even)' (Bell curve (normal)). Explanatory text for duration and effort distribution is provided. The 'PROJECT PARAMETERS' section is partially visible at the bottom.

Project information. Name, status, duration, planned start and the flat / bell-curve choice.

Step 2 — Allocate the sites

Set the **total sites**, then add one **allocation row** per group of sites that share a product, connectivity mode and complexity. The badge turns green when the rows add up to the total — that’s when you can calculate. (A whole site list can be brought in with **Import from Excel**.)



DPM FTE

NETWORK ESTIMATOR

ESTIMATE

Dashboard

WAN Estimator

LAN Estimator

PLAN

Team capacity

DATA

FTE Records

Projects

DPM Directory

HELP

Rates & Method

Settings

Switch to dark

WAN Estimator

Saving to data folder

WAN · 0.52 FTE · 56.3 MD

per site for that product and mode.

Product

SD-WAN

Connectivity mode

Dual vEdge CPE

Sites

0

Complexity %

100

+ Add allocation row

Clear all rows

✓ 25 of 25 sites allocated — ready to calculate

#	PRODUCT	CONNECTIVITY MODE	SITES	COMPLEXITY	BASE RATE MD per site
1	SD-WAN	Dual vEdge CPE	25	100%	2.25
Total			25		

RESULT

✓ WAN result — Acme Logistics — SD-WAN

DPM-ALS-U4R6

Standard mode

FTE REQUIRED

0.52

HEADCOUNT

1 people

UTILISATION

52.1%

TOTAL EFFORT

56.250 MD

Site allocation by product. Each row is *base rate × complexity × sites*. The green badge means the allocation balances.

Step 3 — Read the result

Press **Calculate WAN FTE**. The result shows the headline figures and then **exactly how the number was reached**, step by step — so you can explain or defend any estimate.

file:///C:/Users/fvzh9225/AppData/Local/Temp/claude/C--Users-fvzh9225-OneDrive---orange-com-Bureau-FTE-Website/048ba4fb-171b-4a10-8c... 6/20



DPM FTE

NETWORK ESTIMATOR

ESTIMATE

Dashboard

WAN Estimator

LAN Estimator

PLAN

Team capacity

DATA

FTE Records

Projects

DPM Directory

HELP

Rates & Method

Settings

Switch to dark

WAN Estimator

Saving to data folder

WAN · 0.52 FTE · 56.3 MD

FTE REQUIRED ⓘ

0.52

UTILISATION ⓘ

52.1%

PER MONTH ⓘ

9.375 MD

HEADCOUNT ⓘ

1 people

TOTAL EFFORT ⓘ

56.250 MD

DURATION

6 months

EFFORT BY ROW

SD-WAN — Dual vEdge CPE

2.250 MD/site × 100% × 25 sites = 56.250 MD (100% of total)

HOW THIS NUMBER WAS REACHED

1

Effort for each allocation row

base rate x complexity x sites, summed over 1 row(s)

56.25 MD

2

Total project effort

56.25 MD

56.25 MD

3

Spread across the duration

56.25 MD / 6 months

9.375 MD per month

4

Convert to full-time people

9.375 MD per month / 18 MD capacity per DPM per month

0.521 FTE

5

Round up to whole people

ceil(0.521)

1 headcount

6

Resulting utilisation

52.1%

The result. FTE, headcount, utilisation and total effort up top; the per-row maths and the full working below.

It's already saved

Every calculation is written to your records (and the data folder) automatically. You don't need a "save" button — though you can **Export to Excel** or **Email result** at the bottom.

3 A LAN estimate

A LAN estimate prices local-network rollouts per site from a **device-count tier** (how many devices a site has).

It works like the WAN estimator — name, duration, total sites, then allocation rows — with three differences:

- ✓ **Tiers, not products.** Each allocation row picks a size tier (OD/XS, S, M, Large, XL, Campus). If you add no rows, a **device count** prices the whole project at one tier.
- ✓ **Three calculation modes.** **Standard** uses the published tier rate card; **Non-standard** lets you type your own man-days per site; **By Stage** builds the rate from the delivery stages you select (Design, Planning, Implement, Closing, Controls).
- ✓ **A fallback override** field appears in Non-standard mode for the no-tier-rows case.

The screenshot shows the 'DPM FTE NETWORK ESTIMATOR' interface. The left sidebar contains navigation links: ESTIMATE (Dashboard, WAN Estimator, LAN Estimator), PLAN (Team capacity), DATA (FTE Records, Projects, DPM Directory), and HELP (Rates & Method, Settings). The main content area is titled 'LAN Estimator' and includes a status bar at the top right showing 'Saving to data folder' and 'WAN • 0.52 FTE • 56.3 MD'. Below this, a descriptive text explains that the estimator spreads man-days evenly, while a bell curve shows a normal distribution with a mid-project peak. The 'PROJECT PARAMETERS' section includes input fields for 'Total sites' (60) and 'Device count' (0, labeled 'fallback only'). It also has a 'FLAN used' toggle set to 'recorded only' and a 'Calculation mode' selector with options 'Standard', 'Non-standard', and 'By Stage'. A note states 'Rates come from the published tier rate card.' The 'ASSIGNED DPMS' section shows 'USED IN THE TEAM PLAN' and a '+ Assign DPMS' button, with a message: 'No DPMS assigned yet. Assignments are recorded on the estimate and included in exports.' The 'SITE ALLOCATION BY TIER' section includes buttons for 'From a site list', 'Import from Excel', and 'Template'. It provides instructions: 'Add one row per group of sites in the same size tier. Effort for a row is **base rate × complexity × sites**. Tiers are determined by how many devices a site has — see **Rates & Method** for the full table.' At the bottom, there are labels for 'Tier' and 'Sites'.

LAN parameters. Total sites, the device-count fallback, and the Standard / Non-standard / By Stage mode selector.

Which mode?

Use **Standard** for normal work. Use **By Stage** when only some delivery stages apply. Use **Non-standard** when you have a negotiated rate the card doesn't cover.

4 Comparing scenarios

Weigh the same project under different conditions — complexity, mode, flat vs bell curve, migration, duration, capacity, the allocation — side by side.

1. Set up the project as usual, then press **+** **Add to comparison** (next to Calculate). That snapshots the current form as a **scenario**.
2. Change one condition and press it again to add another. Repeat for as many as you want to weigh.
3. Read the **Compare scenarios** panel: the conditions that differ from the first (baseline) are highlighted, and each result shows its change against the baseline (e.g. **+50%**).

WAN Estimator Saving to data folder WAN · 0.78 FTE · 56.3 MD

	BASELINE	BELL CURVE	4 MONTHS
CONDITIONS			
Duration	6 months	6 months	4 months
Total sites	25	25	25
Mode	Standard	Standard	Standard
Distribution	Flat	Bell curve	Flat
Migration uplift	No	No	No
DPM capacity	18 MD/mo	18 MD/mo	18 MD/mo
Allocation	SD-WAN — Dual vEdge CPE: 25 @ 100%	SD-WAN — Dual vEdge CPE: 25 @ 100%	SD-WAN — Dual
RESULTS			
Total man-days	56.250 MD	56.250 MD same	56.250 MD same
Per month	9.375 MD	9.375 MD same	14.063 MD +50
FTE required	0.52	0.52 same	0.78 +50%
Headcount	1 people	1 people	1 people
Utilisation	52.1%	52.1%	78.1%
Peak FTE	—	0.82	—
Peak headcount	—	1 people	—

NOTES
Extra notes optional ⓘ
Assumptions, caveats, context for the reviewer... — you can add or edit these before or after calculating.

Three scenarios side by side. “Bell curve” and “4 months” differ from the baseline (highlighted); the 4-month option needs +50% FTE.

- ✓ **Nothing is saved while you experiment** — a scenario is only a what-if.
- ✓ **Load** puts a scenario back on the form to tweak; **↵** renames it; **✕** removes it.
- ✓ When one is right, its **Save** button files it as the real estimate. **Save comparison** keeps the whole set to reopen later with **Open saved**.

5 Records & projects

Two different things are saved for you — and it’s worth knowing which is which.

An FTE record


A calculated result, frozen with the inputs that produced it. One per calculation; never overwritten.

A project


A set of inputs you typed, saved under a name so you can reload and re-estimate later.

FTE Records

Every calculation lands here automatically. Filter by name, creator, type or status; sort; open any record to see its full breakdown; or **Export all to Excel**. The portfolio charts at the bottom total everything saved.

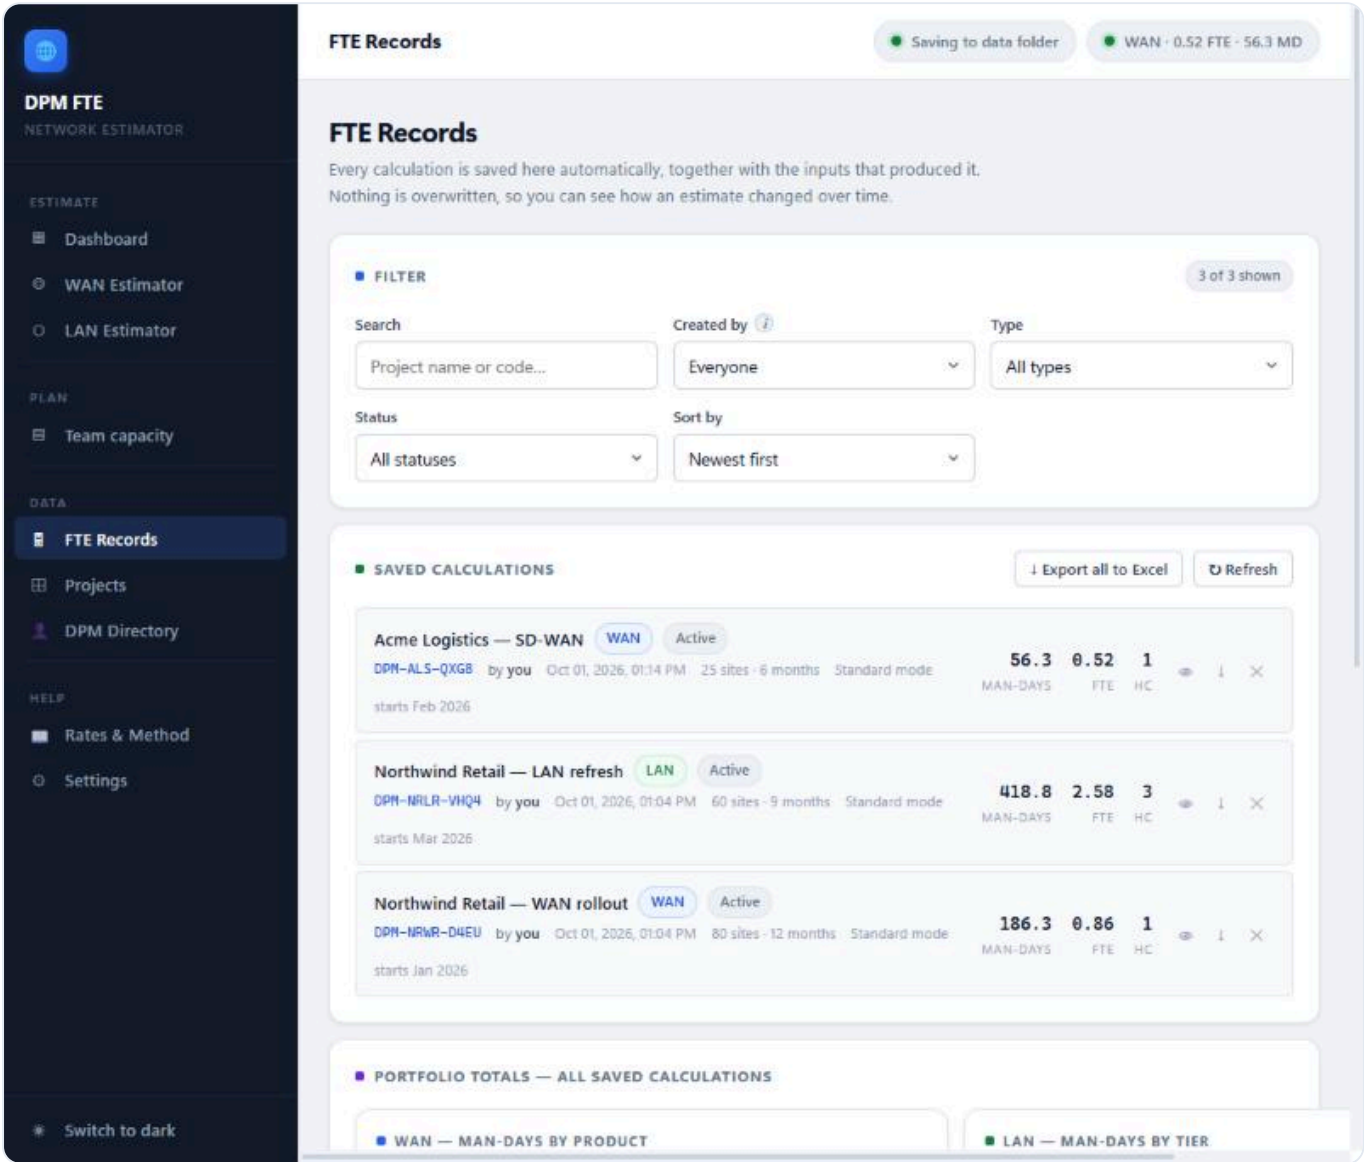


FTE Records. The filter bar, the saved calculations, and each estimate’s man-days / FTE / headcount.

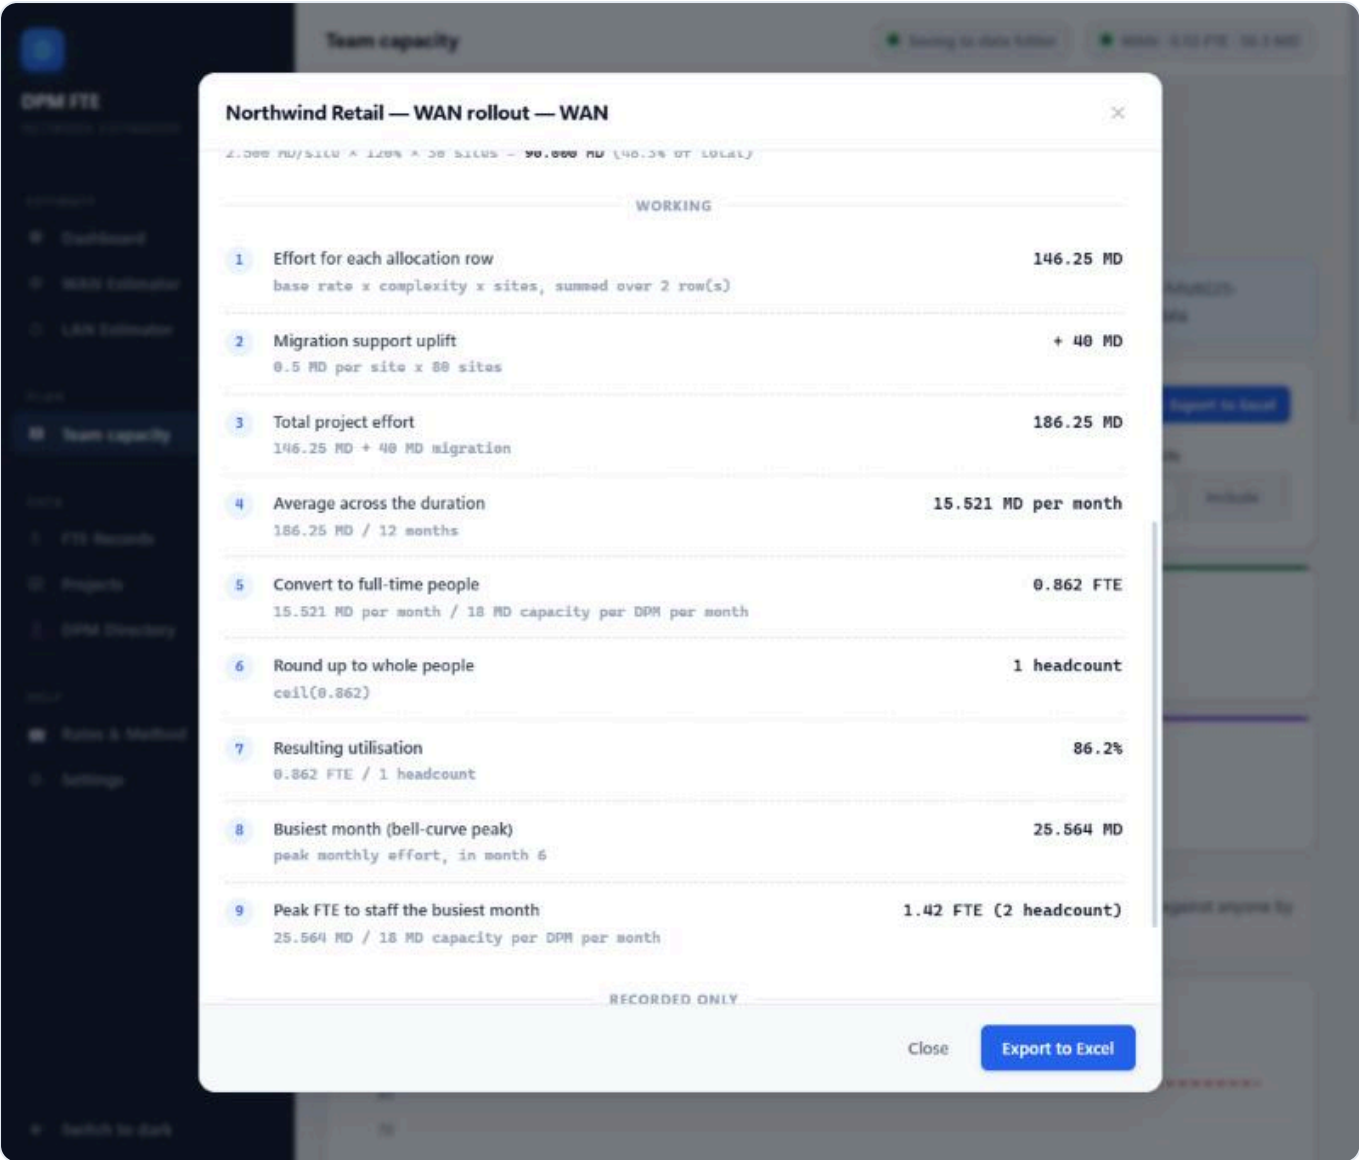

A record’s detail. The same step-by-step working, here showing a migration uplift and the bell-curve **Peak FTE**. **Export to Excel** is one click.

Projects

Use **Save as project** on an estimator to store the settings you’ve entered. Reload them any time with **Load into estimator**.

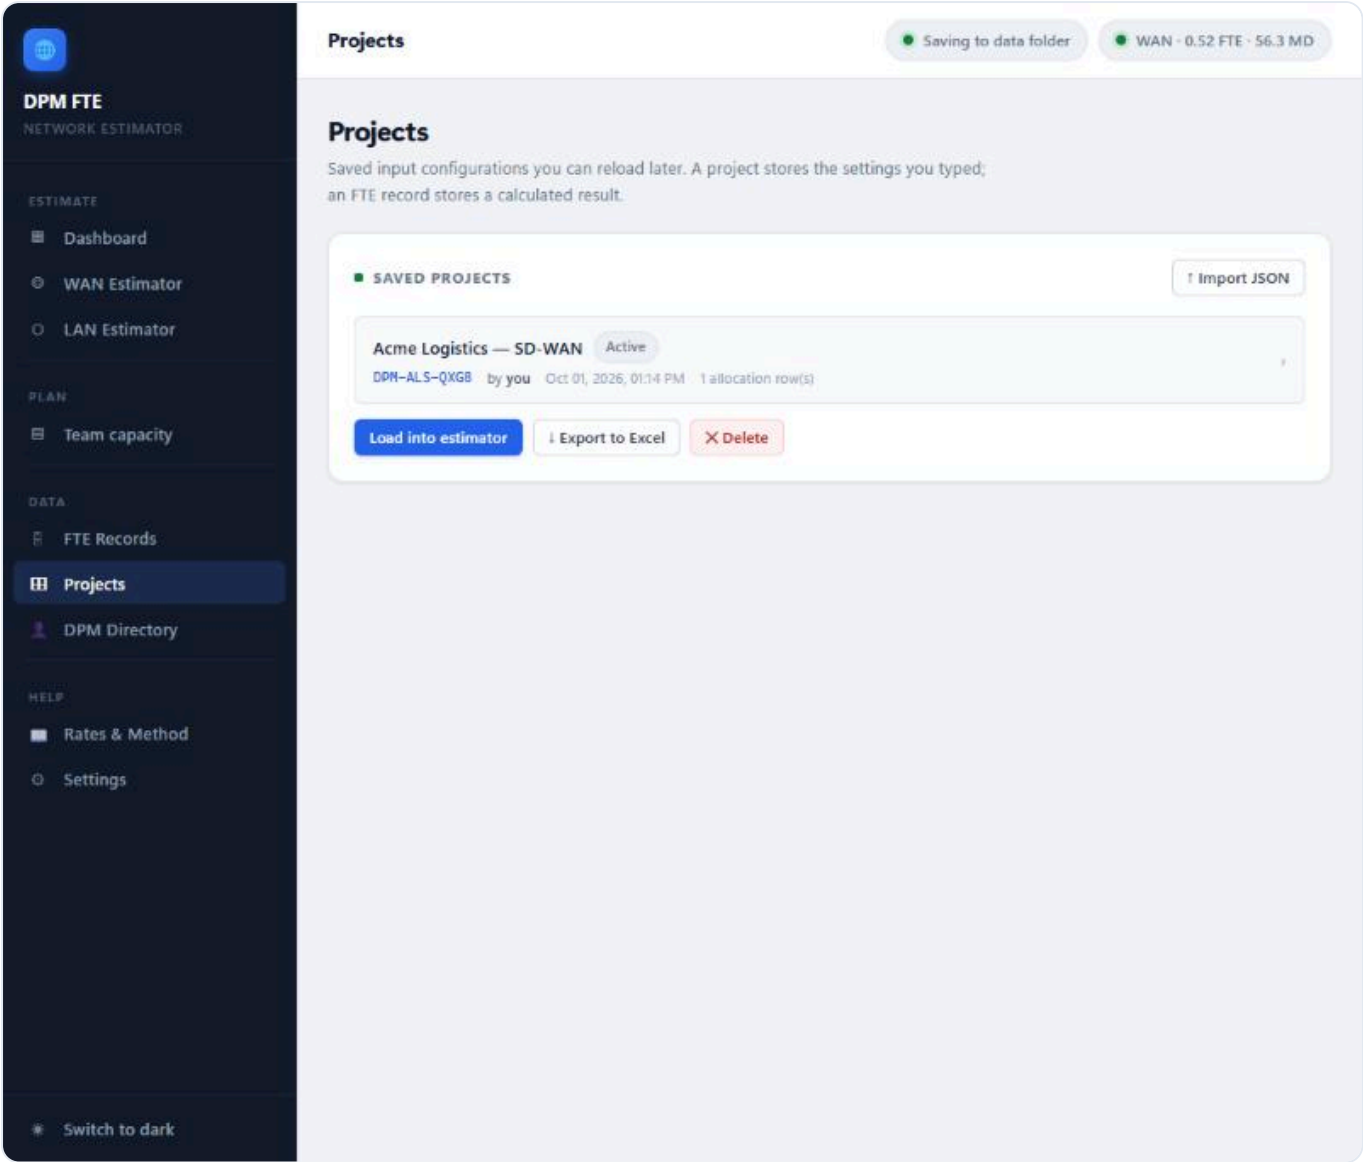


Projects. Saved input configurations you can reload, export or delete.

6 Team capacity

Every active estimate, placed on the calendar from its planned start and added up month by month, compared with the size of the team — so overbooked months show up before they happen.

Set the window (when it starts and how many months to show) and the team capacity. The cards summarise the **team capacity**, the **peak demand** and any **overbooked months**; the chart plots monthly demand against the capacity line.

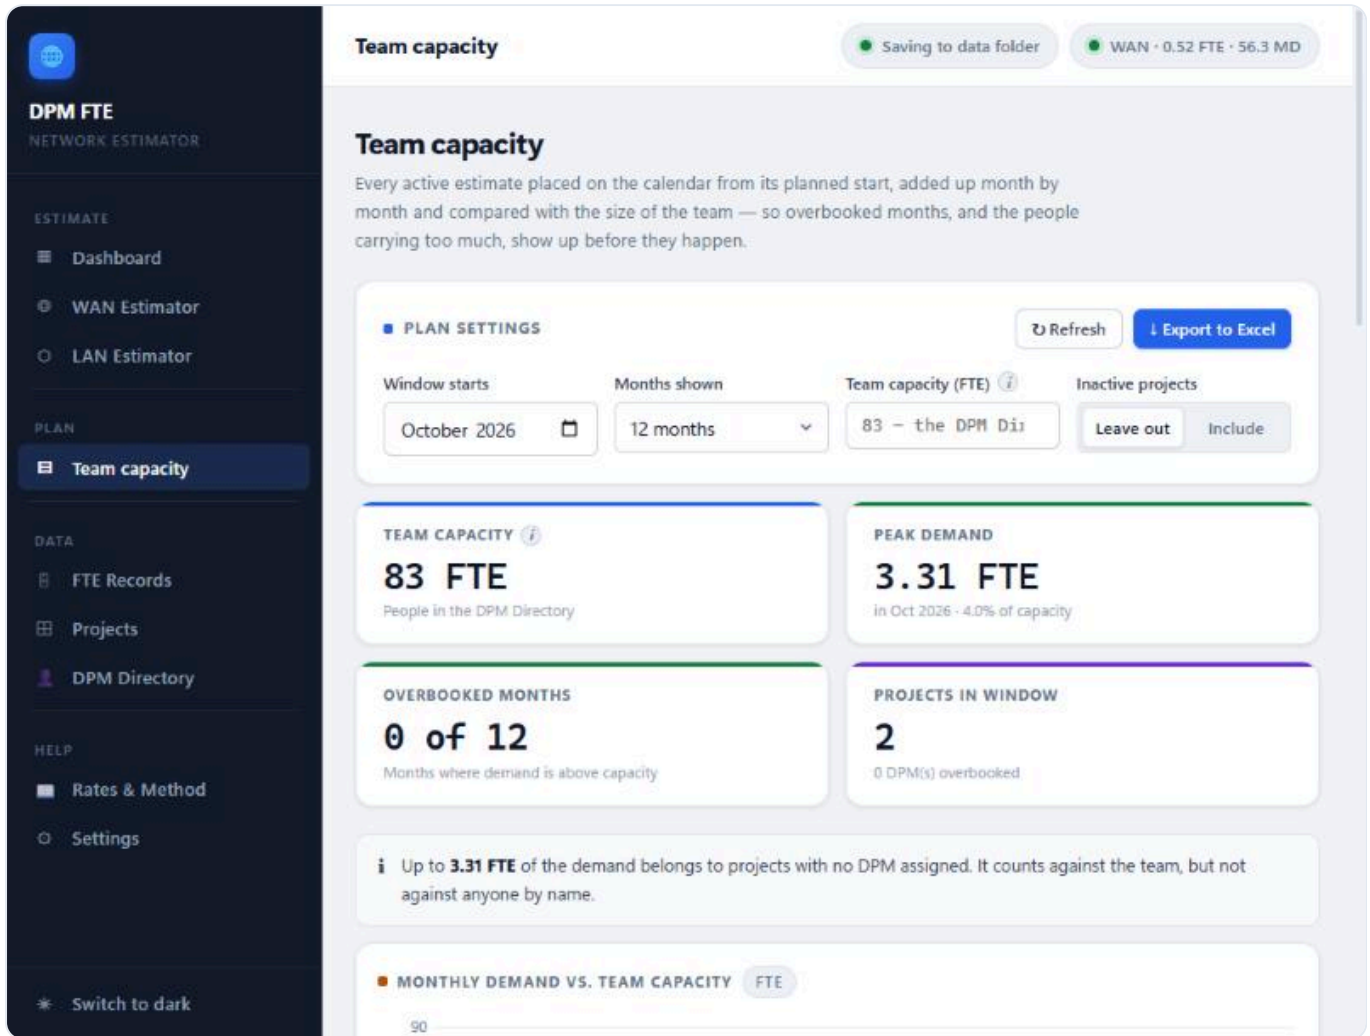

Team capacity. Demand built from every active estimate vs. the team's capacity, with the busiest month called out.

- ✓ Only estimates with a **planned start** and **Active** status appear on the plan.
- ✓ Assign DPMs to an estimate (on the estimator) to see each person's load by name; unassigned demand still counts against the team.

7 The DPM directory

The people you can assign to an estimate.

The directory ships with the team pre-loaded. You can add, edit or remove people, import a list (JSON or a two-column CSV), or export the current one. Your changes live in your browser and never change anyone else's copy; **Restore published list** puts it back to what the app shipped with.

The screenshot displays the 'DPM Directory' interface. On the left is a dark sidebar with navigation links: DPM FTE NETWORK ESTIMATOR, ESTIMATE (Dashboard, WAN Estimator, LAN Estimator), PLAN (Team capacity), DATA (FTE Records, Projects, DPM Directory), and HELP (Rates & Method, Settings). A 'Switch to dark' toggle is at the bottom. The main content area is titled 'DPM Directory' and includes status indicators: 'Saving to data folder' and 'WAN · 0.52 FTE · 56.3 MD'. Below the title is a description: 'The people who can be assigned to an estimate. Assignments are recorded on the estimate and included in exports.' A 'MANAGE THE LIST' section contains buttons for '+ Add DPM', 'Import', 'JSON', and 'Excel'. A text box explains that changes are saved in the browser and provides an example JSON array: `{ "name": "...", "email": "..." }`. A search filter 'Filter by name or email' with a 'Start typing...' input is present. The main list, titled 'ALL DPMS 83 OF 83', shows a grid of people cards. Each card displays a name and an email address. A 'Restore published list' link is in the top right of the list area.

ALL DPMS 83 OF 83			Restore published list
Abanoub Wasfy abanoub.wasfy.ext@orange.com	Abdelrahman Sadek abdelrahman.sadek.ext@orange.com	Ahmed Danish ahmed.danish.ext@orange.com	
Ahmed Elbourgy ahmed.elbourgy.ext@orange.com	Ahmed Elhadidy ahmed1.elhadidy.ext@orange.com	Ahmed ElKhateeb ahmed.elkhateeb.ext@orange.com	
Ahmed Hweedy ahmed.hweedy.ext@orange.com	Ahmed Mohey ahmed.mohey@orange.com	Ahmed Osama ahmed.o.osama.ext@orange.com	
Ahmed Raslan	Aliaa Medhat	Aly Maher	

DPM Directory. Search, add or import people; each is available to assign on an estimate.

8 Rates & method

Where every number comes from — no hidden maths.

The **Rates & Method** page lists the published rate cards (WAN per product and connectivity mode; LAN per tier), the By-Stage activity hours, a worked example, and a glossary of every term. Every result in the app also shows its own arithmetic step by step, so the method is never a black box.

Rates & Method

Saving to data folder | WAN · 0.52 FTE · 56.3 MD

ACTIVITY	OD/XS	S	M	LARGE	XL	CAMPUS
Service implementation set-up	2	2	2	2	2	2
Kick-off / scoping workshop(s)	2	2	3	3	4	8
Awareness	1	1	1	1.5	2	4
Customer communications (local site)	0.5	0.5	1	1.5	2	2
Validate solution design	0.5	0.5	0.5	1	1.5	2
Total hours per site	6	6	7.5	9	11.5	18
Equivalent man-days per site	0.750	0.750	0.938	1.125	1.438	2.250

GLOSSARY

TERM	MEANING
MD - Man-Day	One person working for one full day. The unit all effort in this tool is expressed in.
FTE	Full-Time Equivalent. The number of full-time people needed to carry the monthly workload. Calculated as man-days per month divided by monthly capacity.
HC - Headcount	FTE rounded up to whole people. 2.34 FTE means 3 headcount.
Utilisation	FTE divided by headcount, as a percentage. Shows how fully the rounded-up team is loaded.

Rates & Method. The LAN delivery-stage hours per tier, and the glossary.

The core formula

```
row effort = base rate (MD/site) × complexity % × sites
total      = sum of rows (+ migration uplift on WAN)
per month  = total ÷ duration in months
FTE        = per month ÷ DPM monthly capacity (18 MD)
headcount  = FTE rounded up to whole people
```

You can change the capacity, the migration uplift and the default complexity under **Settings → Calculation assumptions**. Changes apply to *new* calculations only — saved records keep the values that were in force when they ran, so old results stay reproducible.



DPM FTE
NETWORK ESTIMATOR

ESTIMATE

Dashboard

WAN Estimator

LAN Estimator

PLAN

Team capacity

DATA

FTE Records

Projects

DPM Directory

HELP

Rates & Method

Settings

Switch to dark

Settings

Saving to data folder

WAN · 0.52 FTE · 56.3 MD

⚠ Changing these affects **new** calculations only. Every saved record keeps the values that were in force when it ran, so old results stay reproducible.

DPM monthly capacity (MD) ⓘ

18

Productive man-days one full-time DPM delivers per month. Default 18.

Migration uplift (MD per site)

0.5

Added per site on WAN projects when migration support is in scope. Default 0.5.

Default complexity %

100

Pre-filled on new allocation rows. Default 100.

Save settings

Restore defaults

■ EMAIL RESULT — RECIPIENTS

Used by the **Email result** button on the WAN and LAN pages. Change these any time. The email opens as a draft for you to review — it is never sent automatically.

To ⓘ

CC

Subject

leave blank to fill in Outlook

karim.elzarka.ext@orange.com

DPM FTE Estimate - {project}

Separate multiple addresses with a semicolon.

Copied on every result email.

{project} is replaced with the project name.

Save email settings

Restore defaults

■ BACKUP AND TRANSFER

Download everything as a single JSON file you can keep, email, or load into another browser or another machine. Importing adds to what is already here rather than replacing it, and skips anything already present.

Settings. The calculation assumptions, the result-email recipients, and backup / transfer.

file:///C:/Users/fvhz9225/AppData/Local/Temp/claude/C--Users-fvhz9225-OneDrive---orange-com-Bureau-FTE-Website/048ba4fb-171b-4a10-8...

17/20

9

Saving to the SharePoint team folder

So the whole team works from one shared set of estimates, without anyone typing a path.

When you run the app with its launcher, it looks for the shared SharePoint folder “**FTE - Website**” once OneDrive has synced it to your PC, and links it automatically. The chip at the top-right then reads **Saving to SharePoint**. Every estimate is written there as a file and uploaded by OneDrive, and each project gets its own folder holding its estimates and an Excel workbook named `<Project> - <who did it>`.

To get connected (once)

1. Open the team’s “**FTE - Website**” folder on SharePoint.
2. Choose **Add shortcut to My files** — OneDrive syncs it to your PC within a minute or so.
3. Start the app with **Start FTE Calculator.cmd**. It links the folder by itself; the chip shows **Saving to SharePoint**.

Until it’s linked

Estimates save to a folder on your own PC and nothing is lost — they move to the shared folder the moment it’s linked. You can also link it by hand from **Settings**.

One version for everyone

The shared folder records the oldest app version allowed to save into it. A copy that’s too old will say so and ask to be updated rather than save the wrong way — which is what the next chapter is about.

10 Keeping the app up to date

Everyone on the same version, with one click.

The top of the Dashboard shows what the current version added and whether a newer one has been published. The app also checks by itself when it starts, every half hour, and when you come back to it; a chip appears in the top bar when an update is available.

The screenshot shows the DPM FTE Network Estimator Dashboard. The left sidebar contains navigation links: ESTIMATE (Dashboard, WAN Estimator, LAN Estimator), PLAN (Team capacity), DATA (FTE Records, Projects, DPM Directory), and HELP (Rates & Method, Settings). The main content area has a top bar with 'Dashboard', 'Saving to data folder', and 'LAN · 2.58 FTE · 418.8 MD'. Below this is a 'What's new in version 2.3.0' panel with a 'new' tag and a 'Check for updates' button. The panel lists three new features: comparing scenarios side-by-side, adding scenarios with one click, and saving estimates or comparisons. A status bar at the bottom of the panel says 'You have the latest version. Last checked 12:54 PM.' with 'Got it' and 'All updates' buttons. Below the 'What's new' panel is the 'Dashboard' section, which displays the 'LATEST WAN ESTIMATE' with four key metrics: TOTAL MAN-DAYS (186.3), MAN-DAYS PER MONTH (15.5), FTE REQUIRED (0.86), and HEADCOUNT (1 x 86.2%).

What's new in version 2.3.0 new Check for updates

Compare scenarios side by side · released Oct 01, 2026

- Compare scenarios: run several estimates of the same project side by side under different conditions - complexity, mode, flat or bell curve, migration, duration, capacity, the allocation - and see how the man-days and FTE change, with the differences highlighted and the change against the first scenario shown.
- Add a scenario with one click on the WAN or LAN page. Nothing is written to the data folder while you experiment; load any scenario back to tweak it.
- Save the one you want as the estimate, or save the whole comparison in your browser to reopen later.

✓ You have the latest version. Last checked 12:54 PM. Got it All updates

Dashboard

The most recent WAN and LAN estimates, and how the effort is spread across the project calendar.

LATEST WAN ESTIMATE

TOTAL MAN-DAYS ⓘ 186.3 80 sites over 12 months	MAN-DAYS PER MONTH ⓘ 15.5 Sustained monthly workload
FTE REQUIRED ⓘ 0.86 At 18 MD per DPM per month	HEADCOUNT ⓘ 1 × 86.2% People needed and how loaded they are

The “what’s new” panel. Check any time, or read what the latest version changed.

- ✓ **With the launcher: Update now** downloads the new version, installs it and restarts — your estimates and settings are kept.
- ✓ **On the website:** it simply asks you to reload.
- ✓ If a page was open while the app updated, or the folder needs a newer version, the app tells you exactly what to do — reload, restart the launcher, or update.

That's everything

You now know every screen. When in doubt, remember the tool always shows its own working — so you can trust, check and explain any number it produces.
